


Challenge Fund Tranche 2A Blackburn with Darwen Borough Council

ID	Task Mode	Task Name	Predecessors	Duration	Start	Finish	17							06 Mar '17							13 Mar '17							20 Mar '17							27 Mar '17						
							W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S		
1		Prepare CF tranche 2A application		22 days	Wed 01/03/17	Thu 30/03/17																																			
2		Section 151 Officer sign off		0.5 days	Wed 29/03/17	Wed 29/03/17																																			
3		Submit application to Dft	2	0.5 days	Wed 29/03/17	Wed 29/03/17																																			
4		Application assessment by DfT	3	28 days	Mon 03/04/17	Wed 10/05/17																																			
5		<i>Contingency</i>	4	14 days	Thu 11/05/17	Tue 30/05/17																																			
6		Executive member report	5	28 days	Wed 31/05/17	Fri 07/07/17																																			
7		Procurement	5	28 days	Wed 31/05/17	Fri 07/07/17																																			
8		Utility notices	5	28 days	Wed 31/05/17	Fri 07/07/17																																			
9		<i>Contingency</i>	6,7,8	10 days	Mon 10/07/17	Fri 21/07/17																																			
10		Quarterly DfT Report	5	186 days	Mon 26/06/17	Mon 12/03/18																																			
14		Project Board meeting	5	105 days	Thu 01/06/17	Wed 25/10/17																																			
20		Executive Member Briefing	5	106 days	Wed 14/06/17	Wed 08/11/17																																			
27		Stakeholder communications	5	106 days	Wed 21/06/17	Wed 15/11/17																																			
34		A666 Darwen, Excavate & GSB	9	15 days	Mon 24/07/17	Fri 11/08/17																																			
35		Preston New Road	9	10 days	Mon 24/07/17	Fri 04/08/17																																			
36		A666 Darwen,Paving	34	10 days	Mon 14/08/17	Fri 25/08/17																																			
37		Eanam & Higher Eanam, Excavation & GSB	34	8 days	Mon 14/08/17	Wed 23/08/17																																			
38		Eanam & Higher Eanam, Paving	37	10 days	Thu 24/08/17	Wed 06/09/17																																			
39		A666 Whalley New Road, Wilsphire	9	10 days	Mon 24/07/17	Fri 04/08/17																																			
40		<i>Contingency</i>	39	5 days	Mon 07/08/17	Fri 11/08/17																																			
41		A666, Whalley New Road, Roe Lee	40	10 days	Mon 14/08/17	Fri 25/08/17																																			
42		<i>Contingency</i>	41	5 days	Mon 28/08/17	Fri 01/09/17																																			
43		A666, Whalley New Road, Whalley Range	42	10 days	Mon 04/09/17	Fri 15/09/17																																			
44		<i>Contingency</i>	43	5 days	Mon 18/09/17	Fri 22/09/17																																			
45		Lessons Learnt Review	44	1 day	Mon 25/09/17	Mon 25/09/17																																			


Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			

Challenge Fund Tranche 2A Blackburn with Darwen Borough Council

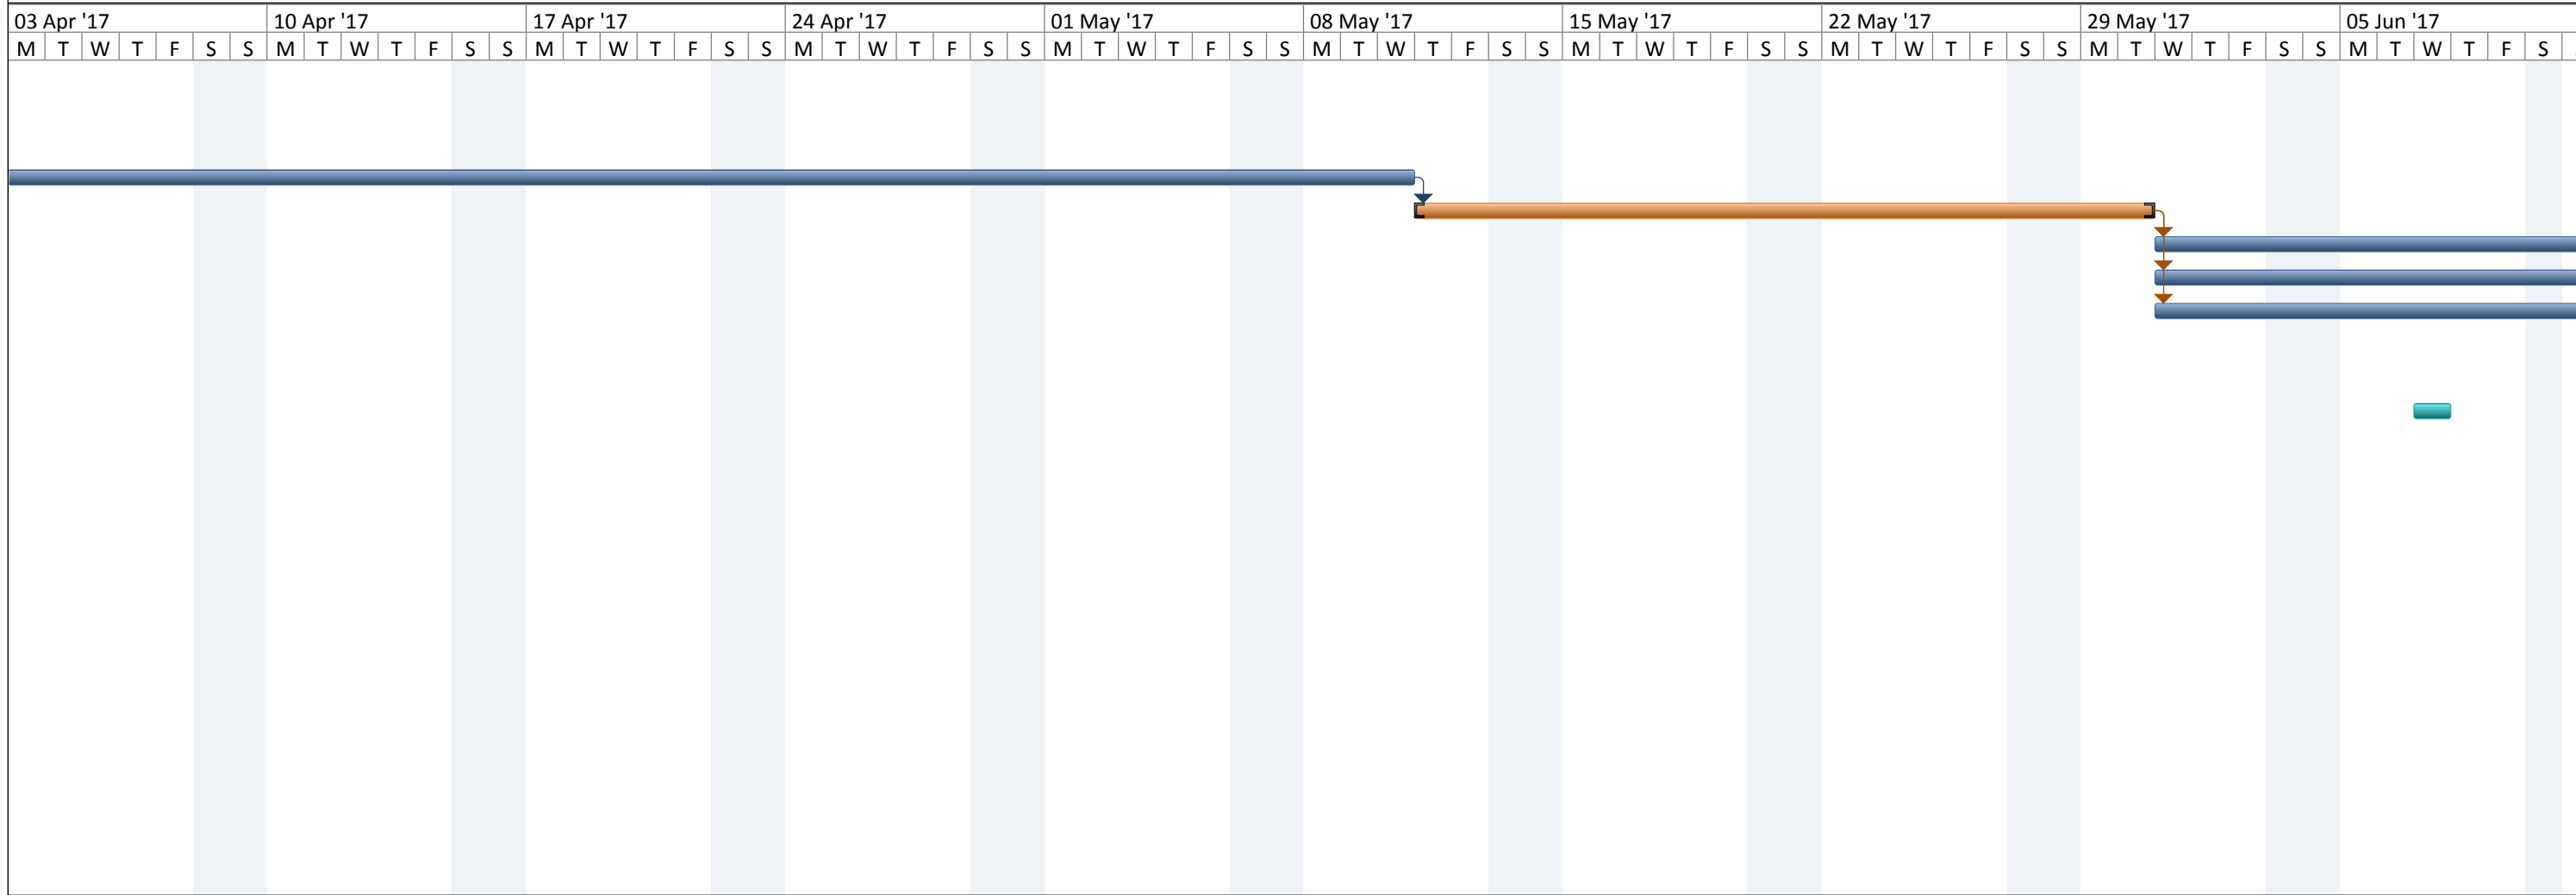


Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			

Challenge Fund Tranche 2A Blackburn with Darwen Borough Council

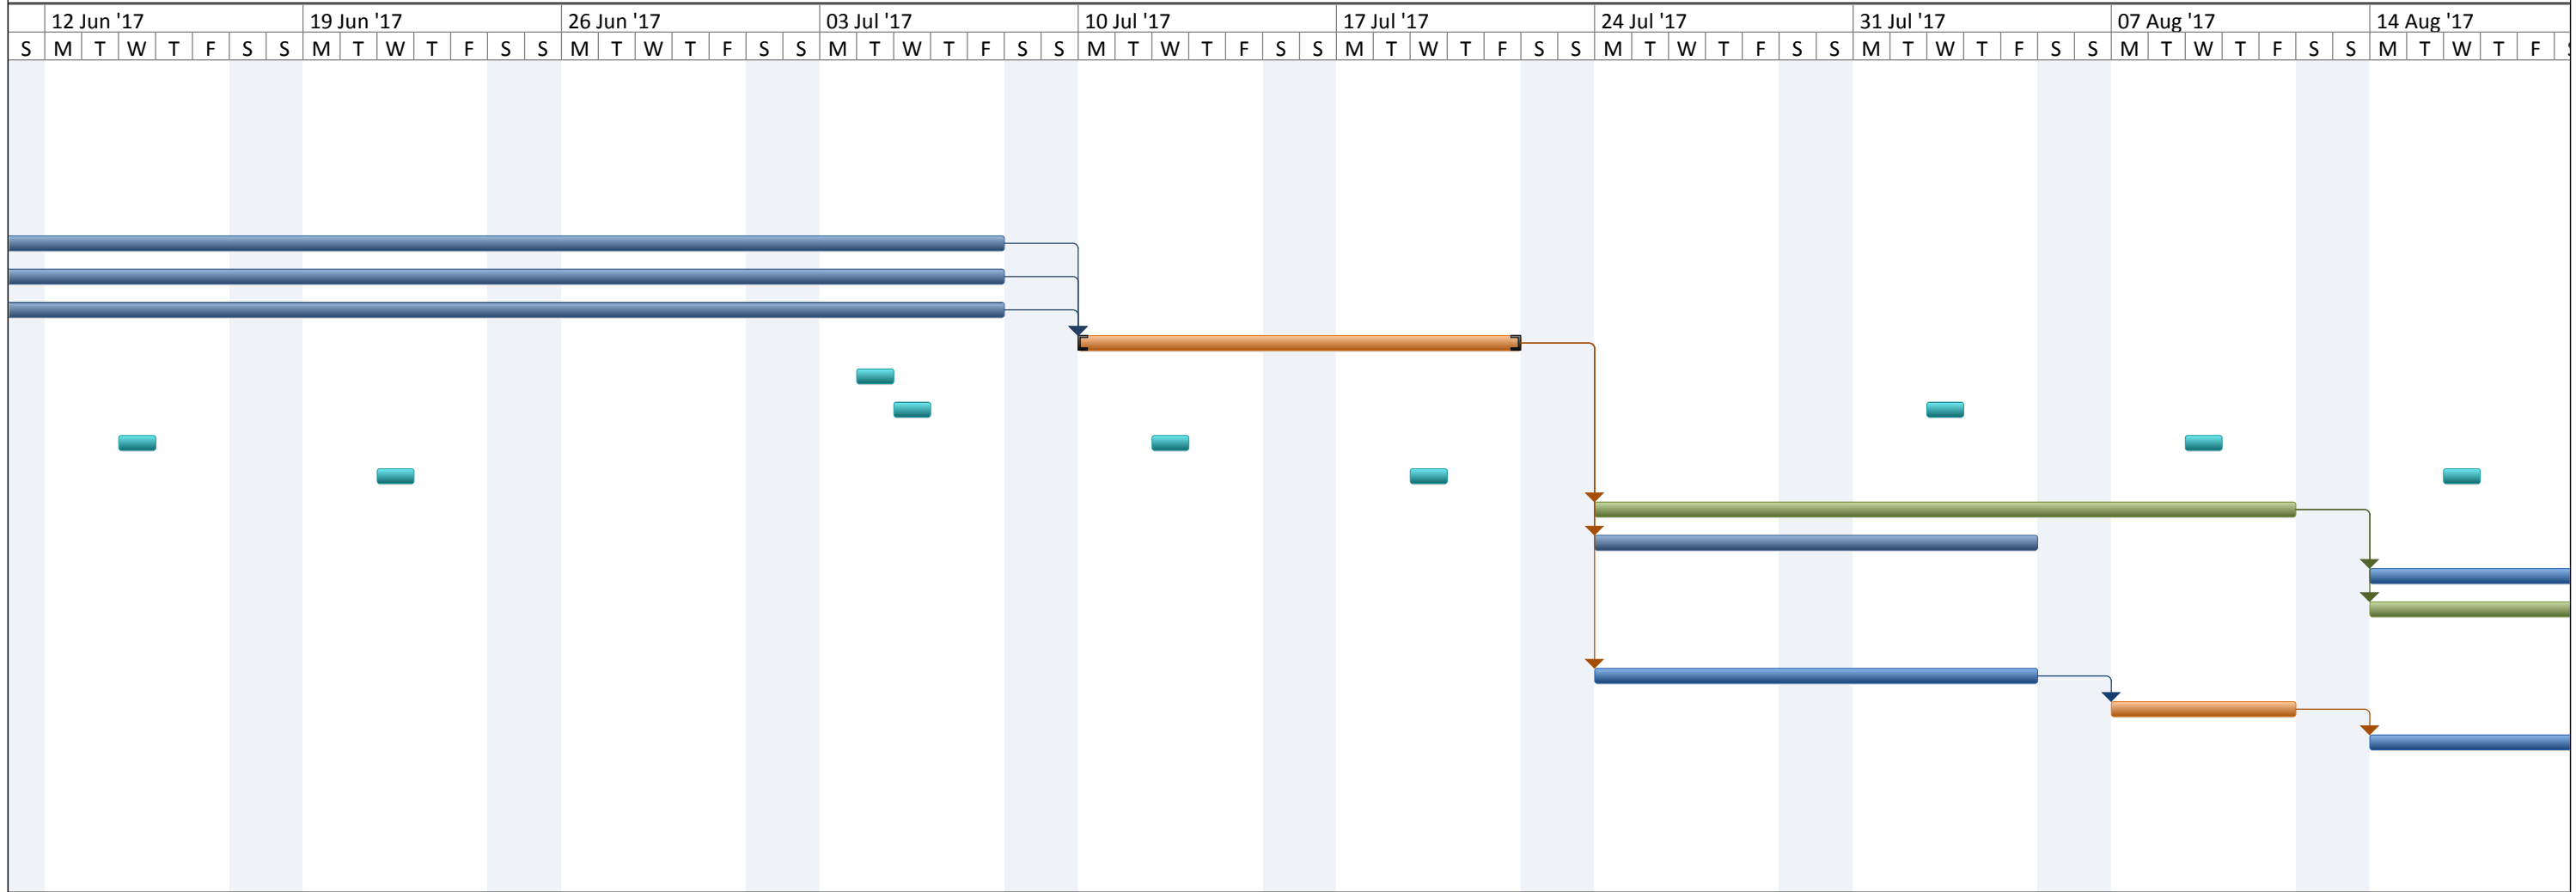


Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			

Challenge Fund Tranche 2A Blackburn with Darwen Borough Council

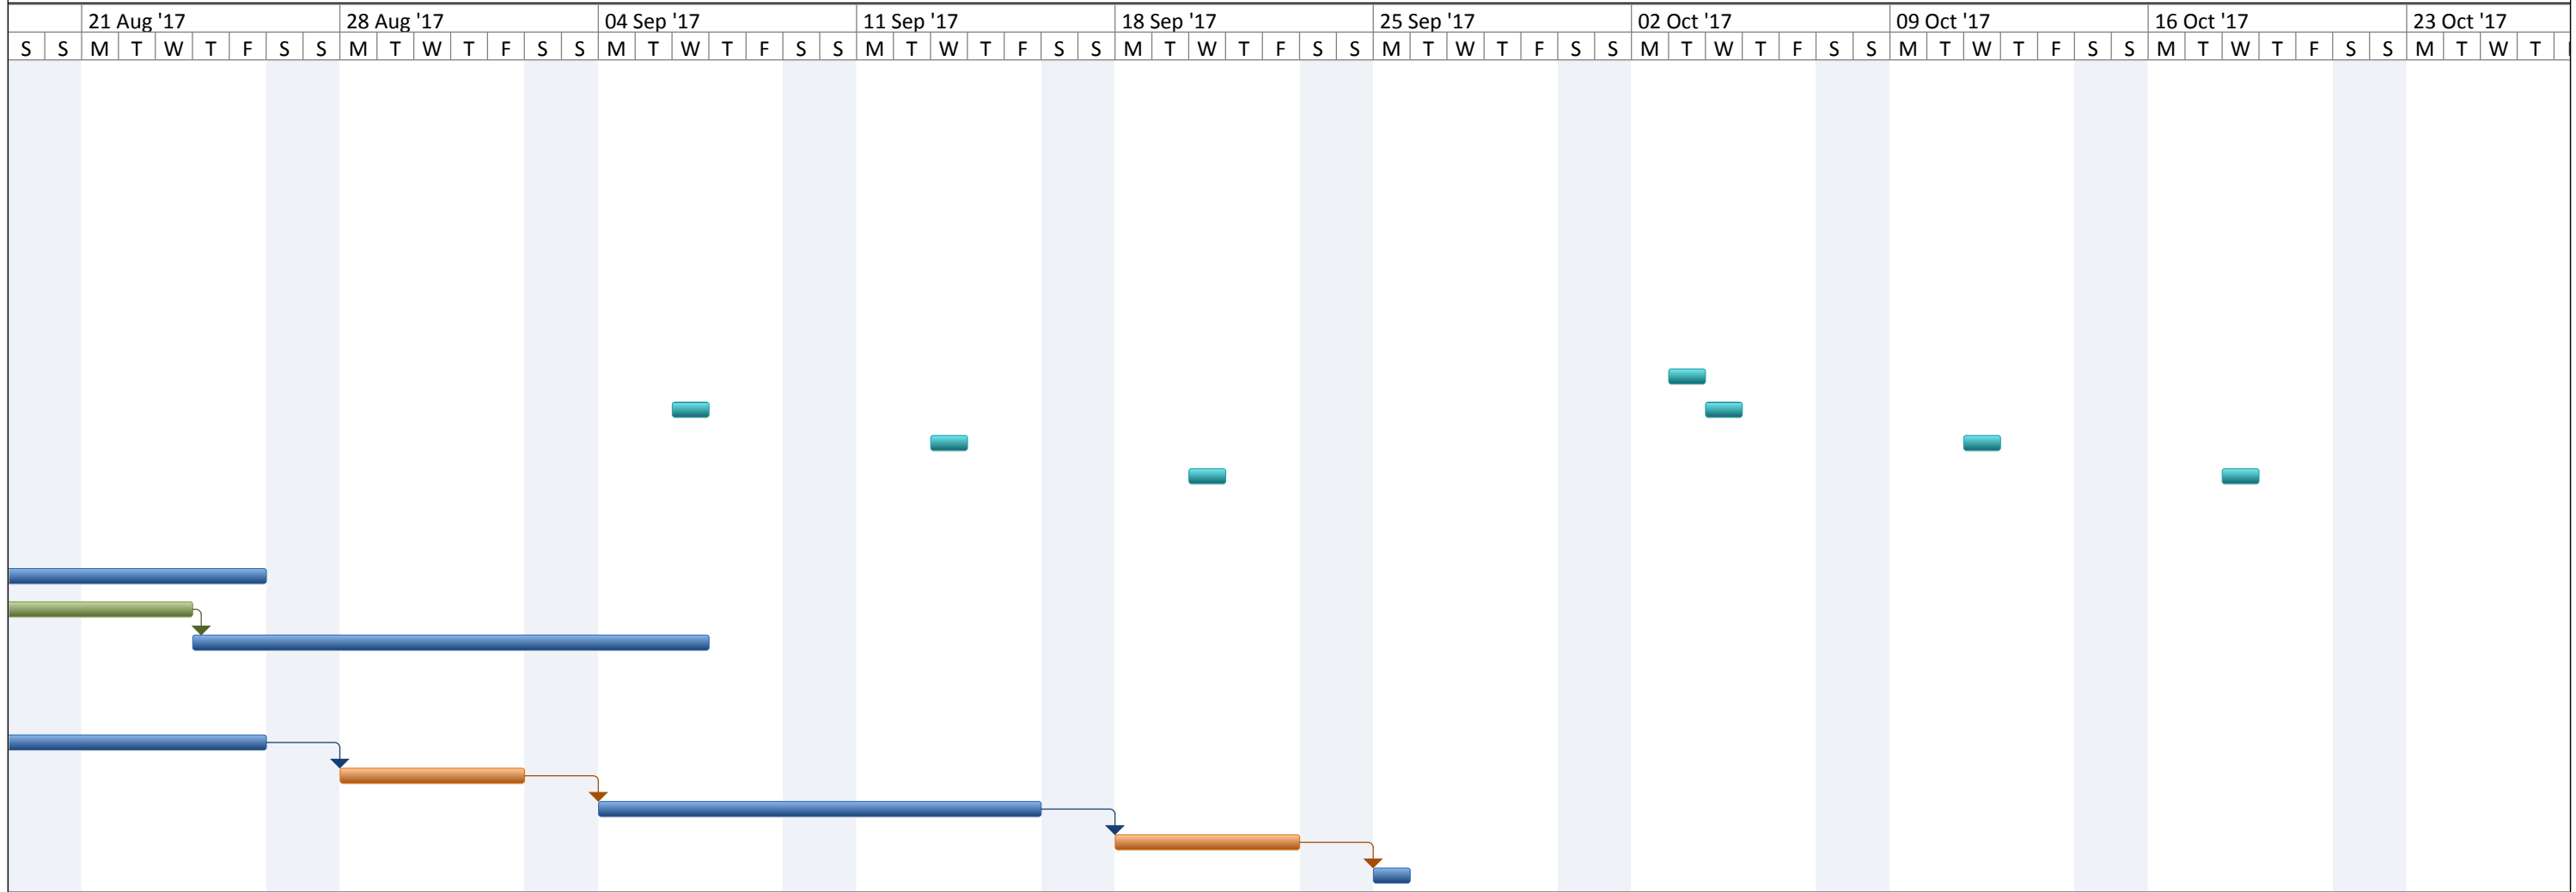


Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			

Challenge Fund Tranche 2A Blackburn with Darwen Borough Council

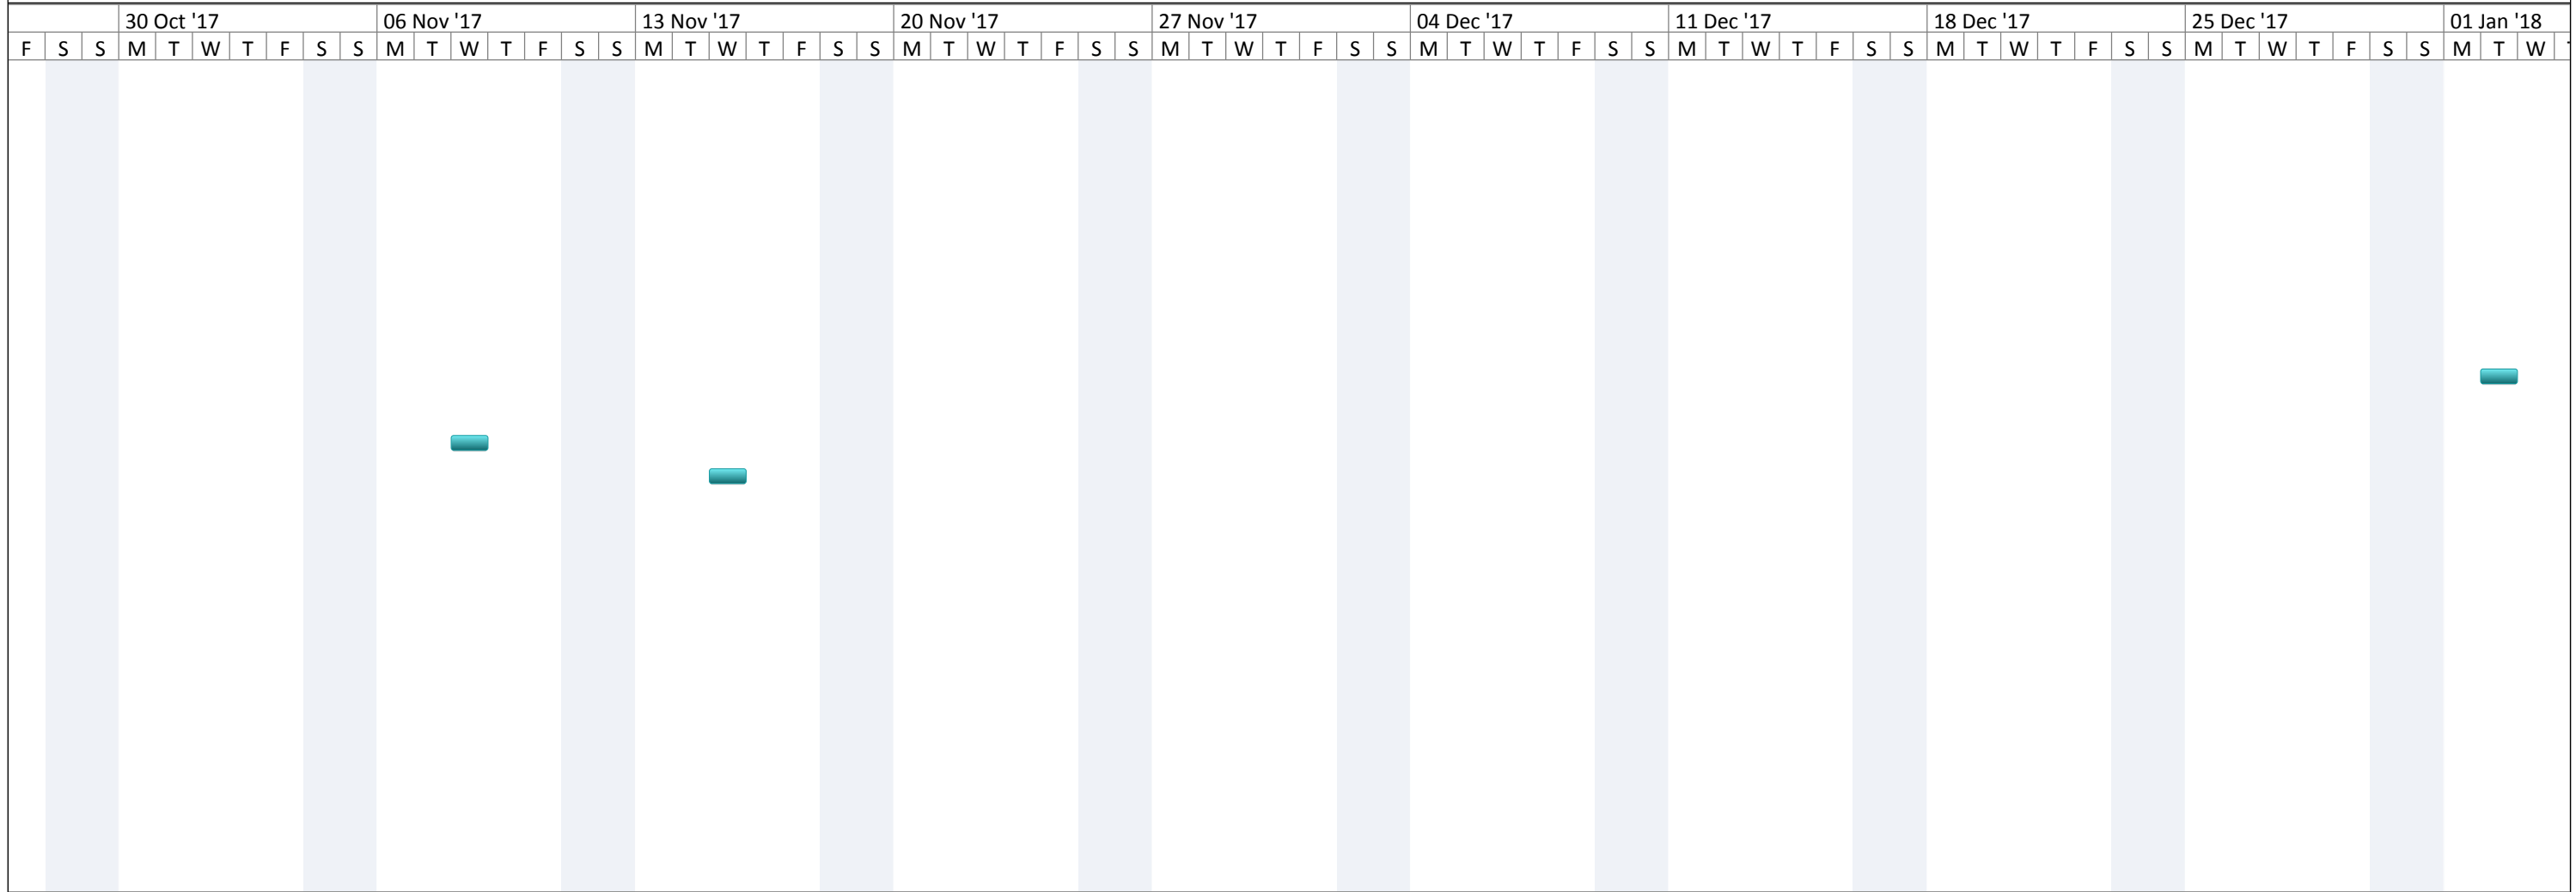

Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			

Challenge Fund Tranche 2A Blackburn with Darwen Borough Council



Project: Tranche2A.mpp Date: Tue 21/03/17	Task		External Tasks		Manual Task		Finish-only		Progress	
	Split		External Milestone		Duration-only		Deadline			
	Milestone		Inactive Task		Manual Summary Rollup		Baseline			
	Summary		Inactive Milestone		Manual Summary		Baseline Milestone			
	Project Summary		Inactive Summary		Start-only		Baseline Summary			
